



ASSIGNMENT 1

Semester 1, 2026

ITPM5.240 Agile Projects

Title	Practical
Type	Project & Online Quiz
Marks	Practical Project – 70 marks Online quizzes – 30 marks
Weighting	70% of final grade
Learning Outcomes	LO1: Apply project management principles and techniques to manage IT/IS projects. LO2: Apply governance and risk management practices when managing IT/IS projects. LO3: Describe the role of project management in software/systems development methodologies.
Deadlines	Individual work Beginning of Week 5 - Progress Report Iteration 1 - Quiz 1 Beginning of Week 9 - Progress Report Iteration 2 - Quiz 2 End of Week 12 - Progress Report Iteration 3 - Quiz 3 Group work During Week 14 Handover Practical Project final

The School of Computing has a policy of no late assignments. However, an assignment handed in up to 24 hours late will be marked. A **deduction of 20% of the total marks** available will be made. Any assignments received more than 24 hours late will not be marked but can be used as evidence of completing terms.

Adhering to the course descriptor, please note you need a minimum of 50% for each course assessment; and a weighted average of 50% or more across all summative assessments.

Introduction

The purpose of this assessment is to plan and control a hypothetical software development project (e-commerce), with supporting documentation. All project planning, documentation, and code must be developed, contained and managed in a **GitHub repository**. At this stage of your learning path, you are not expected to be proficient software developers. The focus is on becoming familiar with the processes and tools used to manage a software project rather than on creating functional code.

The main objective is to obtain and apply the project management experience used to develop websites.

This assessment should be completed in groups consisting of **three (3) students only**.

An overall Group mark for Iterations 1 – 3 will be assigned. Each member of the Group will receive an individual mark based on the proportion and quality of their contributions to the Practical Project – using the three (3) Progress Reports and the three (3) Online Quizzes. Please refer to the Rubric at the end of this document for more information.

Detailed Guidelines

Your Group is going to manage an e-commerce website development process. (Please note: If you have an alternative website idea that is of interest to your Group, check with Lecturer if this is possible to use). The e-commerce website files are missing some components and tasks are allocated amongst three (3) members (see Learner Resources in your EIT Online course). Your job is to integrate all the missing parts from your other group members, using GitHub. You will also be completing the other project management techniques by documenting your progress in every Iteration.

1. You must follow all **Iterations 1 – 3** (overleaf) to successfully achieve your Practical Project requirements (see Fig. 1 overleaf). Please make sure you work with your Group members on a single repository. A template GitHub repository will be automatically created for your Group.
2. Submit **Progress Report** as a group at the end of each iteration (Weeks 5, 9, and 12).
3. Next complete the **Online Quiz**. Refer to your EIT Online ITPM5.240 Assessment tab for details.
4. During Week 14 your Group needs to complete and hand over the **Practical Project - final**.

Project Tasks Workflow

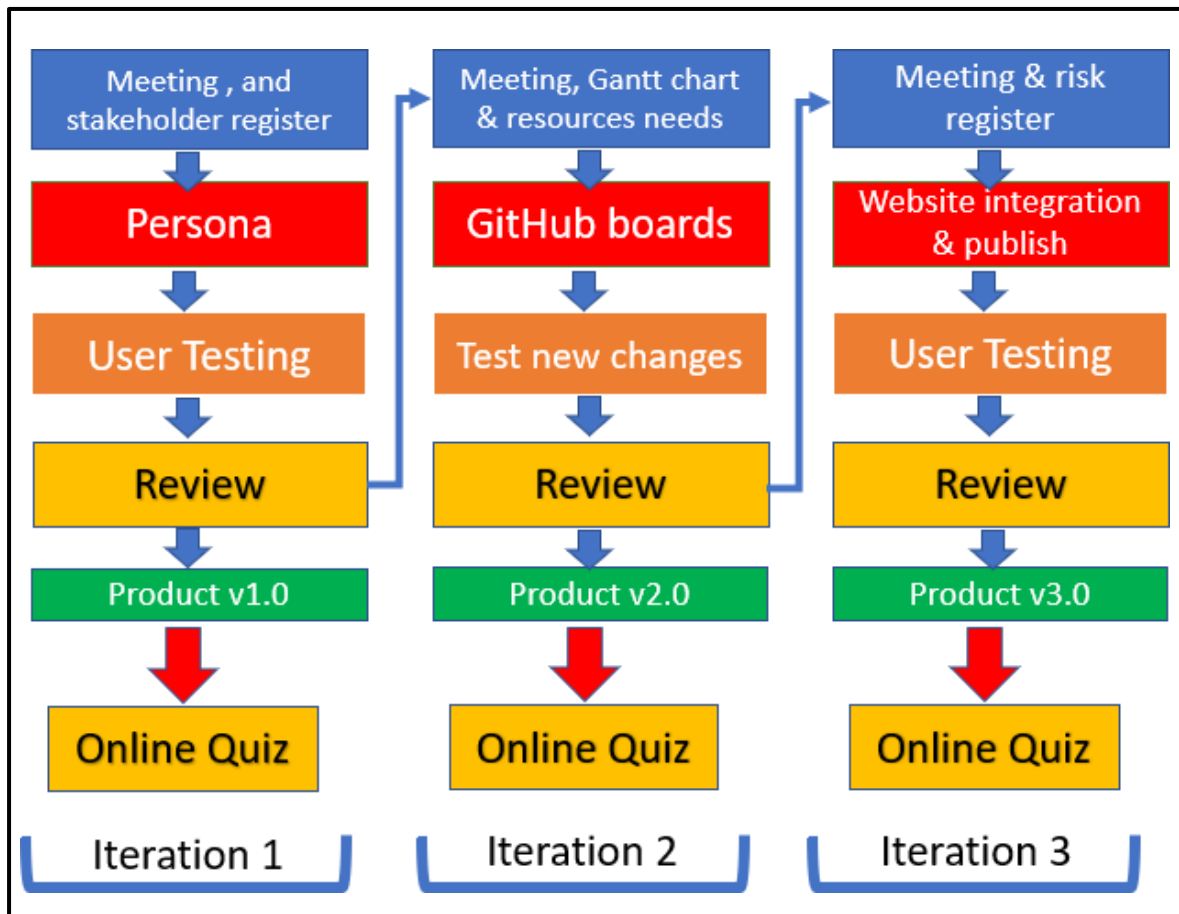


Fig. 1: Overview diagram of project assignment tasks

Iteration 1

(Group work)

- Assign the following tasks within your Group.
- Everyone in the Group must be aware of each step.

Complete by Week 5 (beginning)

Please note – download the course templates from the EIT Online course > Assessments tab

1. Record your weekly meetings for Iteration 1 – use the **Group Meeting Report template**. Make sure you include (meeting agenda, date, meeting actions, attendees, and information about the next meeting).
2. Complete the **Stakeholder Register**. You can use the template provided or create your own. On the register, describe your stakeholders using a list with a role assigned for each in the website development (since no specialist knowledge is required, it is expected that each group member covers each role at some point during the project).
3. Describe at least three (3) different **personas** (fictional characters) that will use your e-commerce website.
4. As a Group, review the three (3) personas. You may wish to include first and final impressions as a user and whether they are relevant.
5. All the above information is to be written on readme.md /Wiki page (or any other files). Please refer to Lab Sessions 1-3 to for information about Git & Markdown language.

Iteration 1: Progress Report

(Group work)

At the end of Iteration 1 you are to complete and submit a group brief Progress Report. (Word count: 150 words).

Submit by Week 5 (beginning)

Use the Assignment link in the EIT Online Assessments tab

1. Explain what you have contributed with your group members (include your completed evidence), and
2. Provide feedback about what's working, what's not working, and what your group needs to improve on as you prepare for Iteration 2.

Online Quiz 1

(Individual work)

- Go to EIT Online course > Assessments tab
- Complete the Online Quiz.

Complete after Iteration 1 Progress Report is submitted

Iteration 2

(Group work)

- Assign the following tasks within your Group.
- Everyone in the Group must be aware of each step.

Complete by Week 9 (beginning)

Please note – download the course templates from the EIT Online course > Assessments tab

1. Record your weekly meetings for Iteration 2 – use the **Group Meeting Report template**. Make sure you include (meeting agenda, date, meeting actions, attendees, and information about the next meeting).
2. As part of your project planning complete a detailed Gantt chart – use the **Gantt Chart template**. It can include (task requirements, start date, end date, and completed by). You are allowed to take a screenshot to include in your markdown. Please note: You will need to submit the actual file in your Handover at the end of Week 13.
3. Refer to your Stakeholder Register and assign the tasks identified in the Gantt chart. Record this information into GitHub boards.
4. Complete a **Resource Requirement List** for the Project. Explain why you need for these resources – include (resource name, description, cost, task code).
5. As a Group, test and review the new changes/readme.md file pushed to GitHub repository. Test the uploaded file and record any issues on GitHub. Make sure all issues are resolved.

Iteration 2: Progress Report

(Group work)

At the end of Iteration 1 you are to complete and submit a group brief Progress Report. (Word count: 150 words).

Submit by Week 9 (beginning)

Use the Assignment link in the EIT Online Assessments tab

1. Explain what you have contributed with your group members (include your completed evidence), and
2. Provide feedback about what's working, what's not working, and what your group needs to improve on as you prepare for Iteration 2.

Online Quiz 2

(Individual work)

- Go to EIT Online course > Assessments tab
- Complete the Online Quiz.

Complete after Iteration 2 Progress Report is submitted

Iteration 3

(Group work)

- Assign the following tasks within your Group.
- Everyone in the Group must be aware of each step.

Complete by Week 12 (end)

Please note – download the course templates from the EIT Online course > Assessments tab

1. Record your weekly meetings for Iteration 3 – use the **Group Meeting Report template**. Make sure you include (meeting agenda, date, meeting actions, attendees, and information about the next meeting).
2. Complete a **Risk Register** to identify and manage actual risks during the progress of your project. Make sure you include (description of risk, likelihood, severity, and a clear resolve plan).
3. Once each Group member has ‘pushed’ the files (Home.html, Orders.html, and Products.html) to GitHub, then merge.
4. Next, check the integration and publish.
(Each page contains a unique code, and all group members need to merge these files on GitHub and test whether they are in a complete format. Please refer to Lab sessions under iteration 3 for information about GitHub merge and GitHub pages).
5. To make sure the project management implementation is successful (good quality, with minimal or no errors), carry out manual user testing, and complete the **User Acceptance Test Results template**.

Iteration 3: Progress Report

(Group work)

At the end of Iteration 1 you are to complete and submit a group brief Progress Report. (Word count: 150 words).

Submit by Week 12 (beginning)

Use the Assignment link in the EIT Online Assessments tab

1. Explain what you have contributed with your group members (include your completed evidence), and
2. Provide feedback about what’s working, what’s not working, and what your group needs to improve on as you prepare for Iteration 2.

Online Quiz 3

(Individual work)

- Go to EIT Online course > Assessments tab
- Complete the Online Quiz.

Complete after Iteration 2 Progress Report is submitted

Practical Project – Final Handover

(Group work)

- Complete and handover the Practical Project as a Group submission into the Assignment Dropbox.

**Submit as a Group
by the end of Week 13**

Your submitted document must include the following:

- ☐ Group Name and Group members
- ☐ A working link to your Group's GitHub repository page
- ☐ A working link to your Group's read.md documentation
- ☐ Downloaded .ZIP file directly from your GitHub, then uploaded your GitHub repository **[optional]**

Evidence for final submission of Practical Project must include:

1. A *complete* readme.md/wiki file on GitHub repository, which documents:
 - a. Group Meeting Reports (for each Iteration 1, 2, 3)
 - b. Stakeholder Register
 - c. Three personas
 - d. Gantt Chart (MS Excel)
 - e. Resource Requirement List
 - f. Risk Register
 - g. User Acceptance Test Results.
2. A *static* website uploaded with GitHub Pages which shows:
 - a. Home page
 - b. Product page
 - c. Order product page.

Academic Requirements

Referencing & Academic Misconduct

- All work submitted must be original and entirely your work, except where you use ideas, quotations, tables, diagrams, code, or any other material from other writers. In such cases, you must acknowledge the source using the APA referencing style.
- No part of the work submitted may be used as part of any assessed work for another academic course.
- Academic misconduct includes dishonest behaviour in the assessment such as copying, cheating and plagiarism, and all other dishonest practices. EIT will treat academic misconduct seriously.
- Section 11 of the Academic Statute lists the penalties for academic misconduct. Penalties range from a warning through to suspension from the programme. All instances of academic misconduct are reported. Read EIT Academic Integrity.

Marking Schedule

As a Level 5 course, the emphasis will be on your ability to demonstrate broad technical and theoretical knowledge within the subject matter.

Marks are allocated for completeness and accuracy of the three tasks with a clear project management application and description.

Completed projects will be marked based on the due date. The rubric below will be used to determine the mark allocation.

Marking Schedule – Rubric

Performance Criteria	Levels of Achievement												Mark
Group Outputs	Outstanding			Accomplished			Competent			Needs improvement			
Iterations: Progress Reports 3 Iterations Found on EIT Online > Assessments	Accurate and comprehensive description of contribution. Demonstrates clearly what's working, what's not working, achievement, issues, and challenges during each iteration.			Mostly accurate and comprehensive description of contribution. Broad description of what's working, what's not working, achievement, issues, and challenges during each iteration			A description of contribution is provided but not sufficient. Partially demonstrates what's working, what's not working, achievement, issues, and challenges during each iteration			Missing Reports, and the description of contribution is limited or not exist. Incomplete information on what's working, what's not working, achievement, issues, and challenges during each iteration			
Iteration	1	2	3	1	2	3	1	2	3	1	2	3	
Marks for each iteration (2 marks each)	2	2	2	1.5	1.5	1.5	1	1	1	0-0.5	0-0.5	0-0.5	/6

Performance Criteria	Levels of Achievement				Mark
GROUP Outputs	Outstanding	Accomplished	Competent	Needs improvement	
Practical Project: Final Handover Documentation on readme.md / Wiki on GitHub repository	A comprehensive description of the documentation. Demonstrates the project follows best practice. Excellent spelling, grammar, and sentence structure. All sources (if any) accurately referenced. Content layout and use of styles are tidy and organised.	A mostly comprehensive description of the documentation. Demonstrates the project follows broad practice. Few minor spelling and grammar errors; sentences generally well structured. Few errors in referencing, but most sources (if any) are accurately referenced in APA format. Content layout and styles are mostly tidy and organised.	Some description provided about documentation, but is superficial (some use of comments, etc.). Some major spelling and grammar errors, some rambling sentences. Most sources (if any) are referenced in APA format but not comprehensive. Content layout and styles lacks some consistency and clarity.	No description included or lacks correct documentation description. Many spelling and grammar errors, major sentence structure issues. Most sources (if any) are not accurately referenced. The content layout and use of styles are chaotic, and disorderly presented.	
	12-11	10-9	8-6	0-5	/12
2a. Meeting Reports (On GitHub)	Three meeting reports submitted (one copy for each iteration). Accurate and comprehensive. Recorded the main actions and agenda.	Three meeting reports submitted (one copy for each iteration). Mostly accurate and comprehensive. Recorded broad actions and agenda.	Three meeting reports submitted (one copy for each iteration). Partially records the main actions and agenda.	Missing meeting reports. Incomplete information on the meeting agenda and actions.	
	6-5	4	3	0-2	/6

2b. Stakeholder Register (On GitHub)	Completed fully and described precisely. GitHub board used effectively to facilitate tasks.	Mostly listed and described. GitHub board used to facilitate majority of tasks.	Partially listed and described. GitHub board used but can be further improved.	Not included or limited. GitHub board has a lot of missing items and/or not effectively identified.	
	5	4	3	0-2	/5
2c. Personas (x 3) (On GitHub)	Accurate and comprehensive personas (x3) designed. Captures bio, motivation, and user requirements.	Mostly accurate and comprehensive personas (x3). Captures bio, motivation, and user requirements.	Two or three personas are designed. Partially captures bio, motivation, and user requirements.	Missing personas. Incomplete information on bio, motivation, and user requirements.	
	6-5	4	3	0-2	/6
2d. Gantt chart (Excel spreadsheet)	Detailed and accurate, using appropriate language. Provides clear and complete format task requirements, start date, end date, and completed by.	Mostly accurate and detailed, using appropriate language. Provides clear format task requirements, start date, end date, and completed by.	A description included. Provides a partial understanding of Gantt chart and relevant information.	No description included. Lacks correct Gantt chart formatting.	
	5	4	3	0-2	/5
2e. Resource Requirement List	Detailed and accurate. Demonstrates complete understanding of resource need analysis. Clear, complete identification of resource name, description, cost, task code.	Mostly accurate and comprehensive. Demonstrates complete understanding of resource need analysis. Complete identification of resource name, description, cost, task code.	Provided but some details missing Partial understanding of resource need analysis. Some identification of resource name, description, cost, task code.	No list is included. Lacks correct understanding of how resource is managed during the project.	
	5	4	3	0-2	/5

2f. Risk Register	Comprehensive, accurate description of risks. Clear resolution plans.	Mostly comprehensive, accurate description of risks. Broad resolution plans.	Almost comprehensive, accurate description of risks. Partial resolution plans.	Not appropriate or not included description of risks.	
	5	4	3	0-2	/5
2g. User Acceptance Test Report	Results and outcomes succinctly explained with corrective action exist.	Results and outcomes explained with corrective action exist.	Results and outcomes explained but not sufficient.	Results and outcomes limited or inappropriate.	
	5	4	3	0-2	/5
Integration Static website on GitHub pages • Home page • Products page • Orders page	Thorough and accurate understanding of agile and website development using VCS – GitHub. Group members actively and equally contributed to integrations and commits. Successfully deployed website, and all pages are working.	Mostly accurate and thorough understanding of agile and website development using VCS – GitHub. Majority of group members contributed to integrations and commits. Successfully deployed website, and most pages are working.	Some understanding of agile and website development using VCS – GitHub. Group members superficially contributed to integrations and commits. Website deployed but major parts are missing.	70	
	15-14	13-11	10-8	0-7	/15
Practical Project: Iterations 1, 2, 3 and Final Handover				49%	/70
Online Quizzes (x3)				21%	/30
Total				70%	/100
